MODERNIZING ENTERPRISE TALENT ACQUISITION

Business Process Analysis & Information System Proposal for an Enterprise ATS

Role: Lead Business Systems Analyst | **Target Audience:** Executive Leadership, VP Talent & CTO

Scope: End-to-End Business Analysis, Architecture, Data Model, Analytics, and Implementation Proposal

Project Baseline	Governance & Compliance	Financial Impact
• Baseline Time-to-Hire: 42 Days • Target Time-to-Hire: 21 Days • 10 Formal Analysis Deliverables • Synthetic Dataset: 1,250 Candidates	• EEOC / OFCCP Compliance Audits • GDPR / CCPA Data Rights • Calibrated Anti-Bias Scorecards • Role-Based Access Control (RBAC)	• Annual Operational Drag: $730,000 • Proposed Net Savings: $525,000/yr • 3-Year Expected ROI: 3.4x • Payback Period: 7.2 Months

Executive Business Case: The Cost of Operational Friction

Legacy hiring operations result in talent leakage, extreme cycle times, and inflated agency reliance.


42 Days Avg Time-to-Hire (vs 22 Ind Avg)	**38% Drop-Off** Candidate Funnel Abandonment	**$4,850** Cost-per-Hire (Excess Agency Fees)	**$730,000** Annual Financial Drag

Key Findings from Operational Discovery:

- **Manual Resume Intake & Disjointed Spreadsheets:** 65% of recruiter effort consumed by data entry, resume parsing errors, and untracked emails.
- **Scheduling Friction Bottleneck:** Coordinating panel interviews takes 4.8 calendar days on average due to back-and-forth manual email exchanges.
- **Delayed Hiring Manager Scorecards:** Average scorecard turnaround is 3.8 days; 30% of top candidates accept competing offers while waiting.
- **Severe Compliance & Reporting Exposure:** No centralized audit log for EEO/OFCCP compliance; manual spreadsheet reporting takes 40+ hours per quarter.

AS-IS Process Baseline: Operational Inefficiencies


Multi-tool fragmentation causes candidate ghosting, data loss, and extended cycle delays.

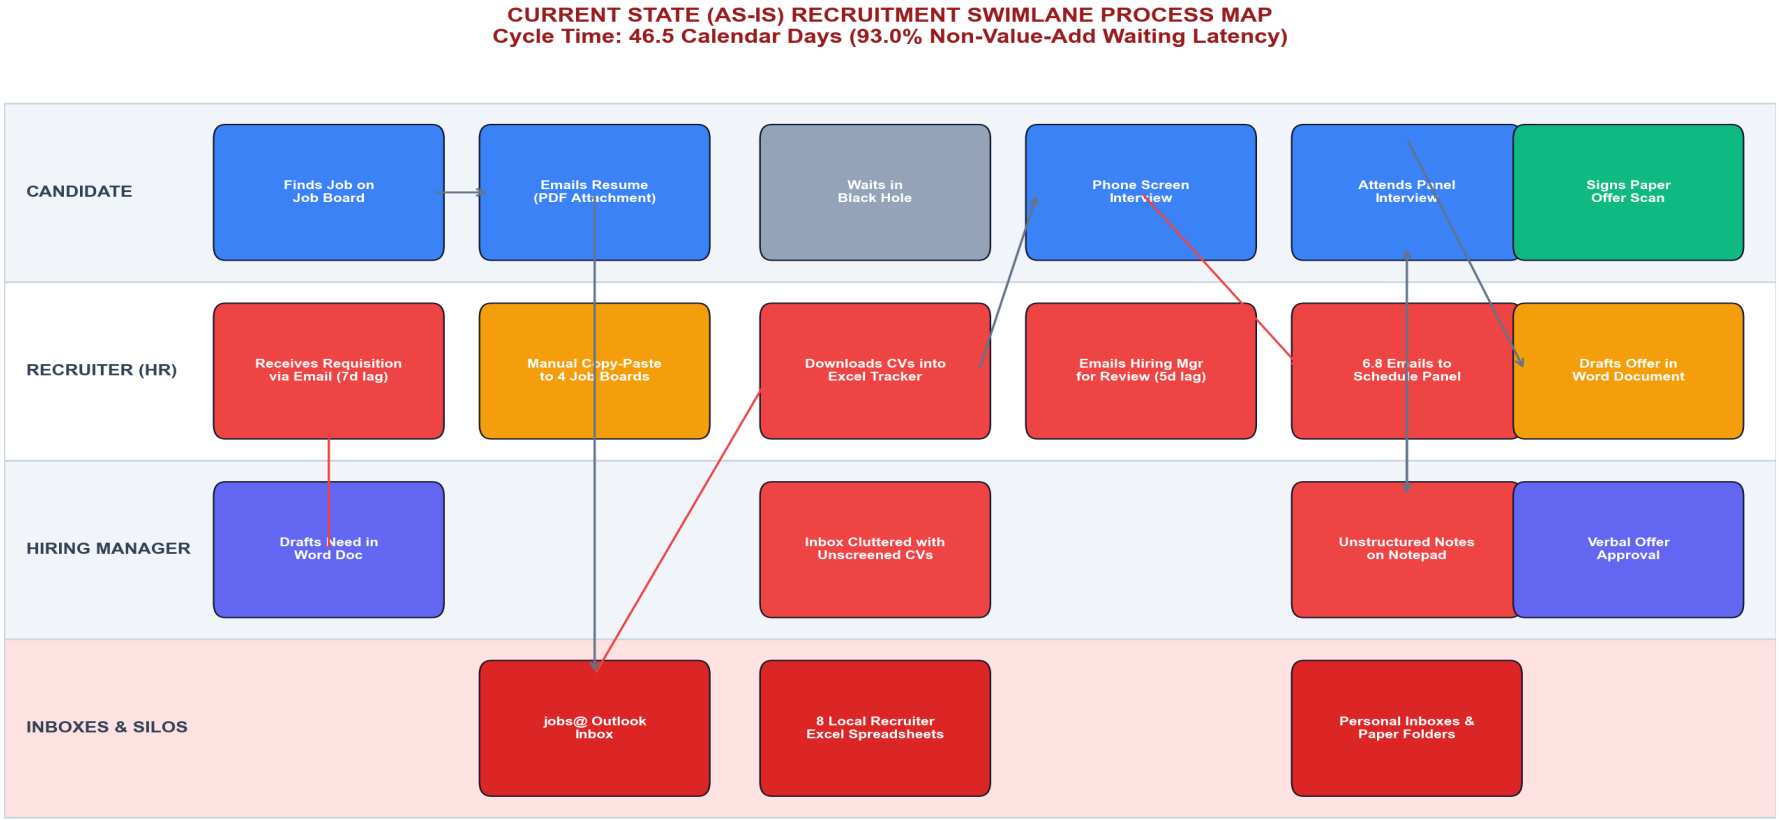

Primary Bottlenecks: Email-based intake | 4.8-day calendar bottleneck | Unstructured interview feedback | High drop-off at screening.

TO-BE Target Operating Model: Automated & Integrated Workflow


Streamlined 5-stage pipeline driven by automated intake, self-service scheduling, and real-time syncing.

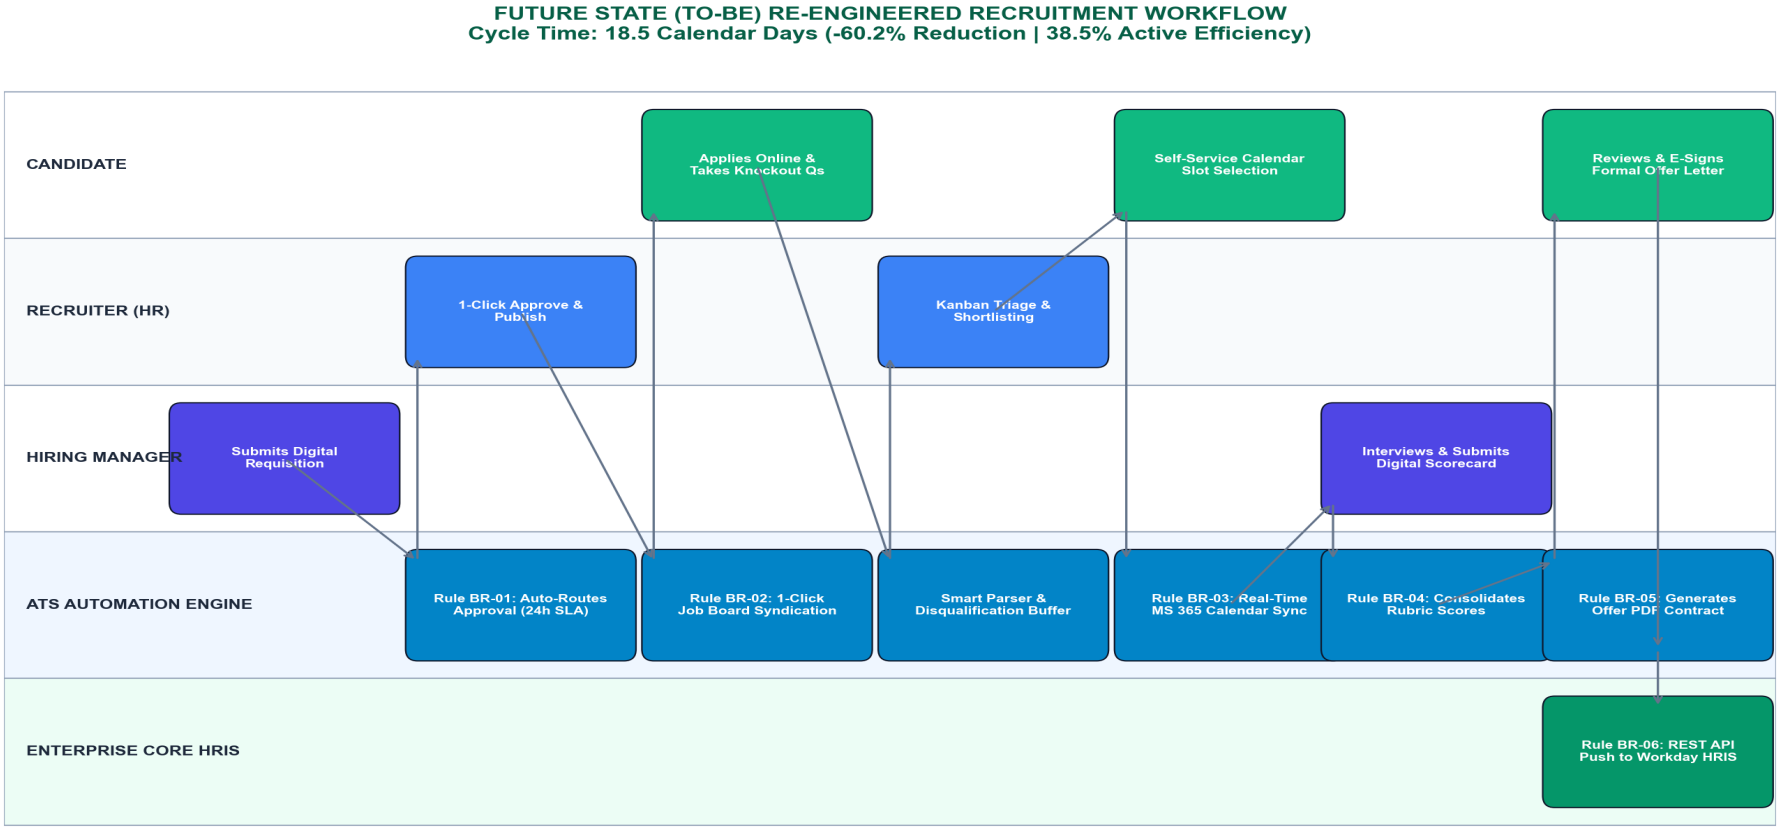

Transformations: Automated resume parsing & knockout scoring | Candidate self-service calendar booking | Mobile rubric scorecards & e-Signatures.

System Requirements & Functional Scope Baseline

Structured into 5 functional modules and validated non-functional architectural baselines.

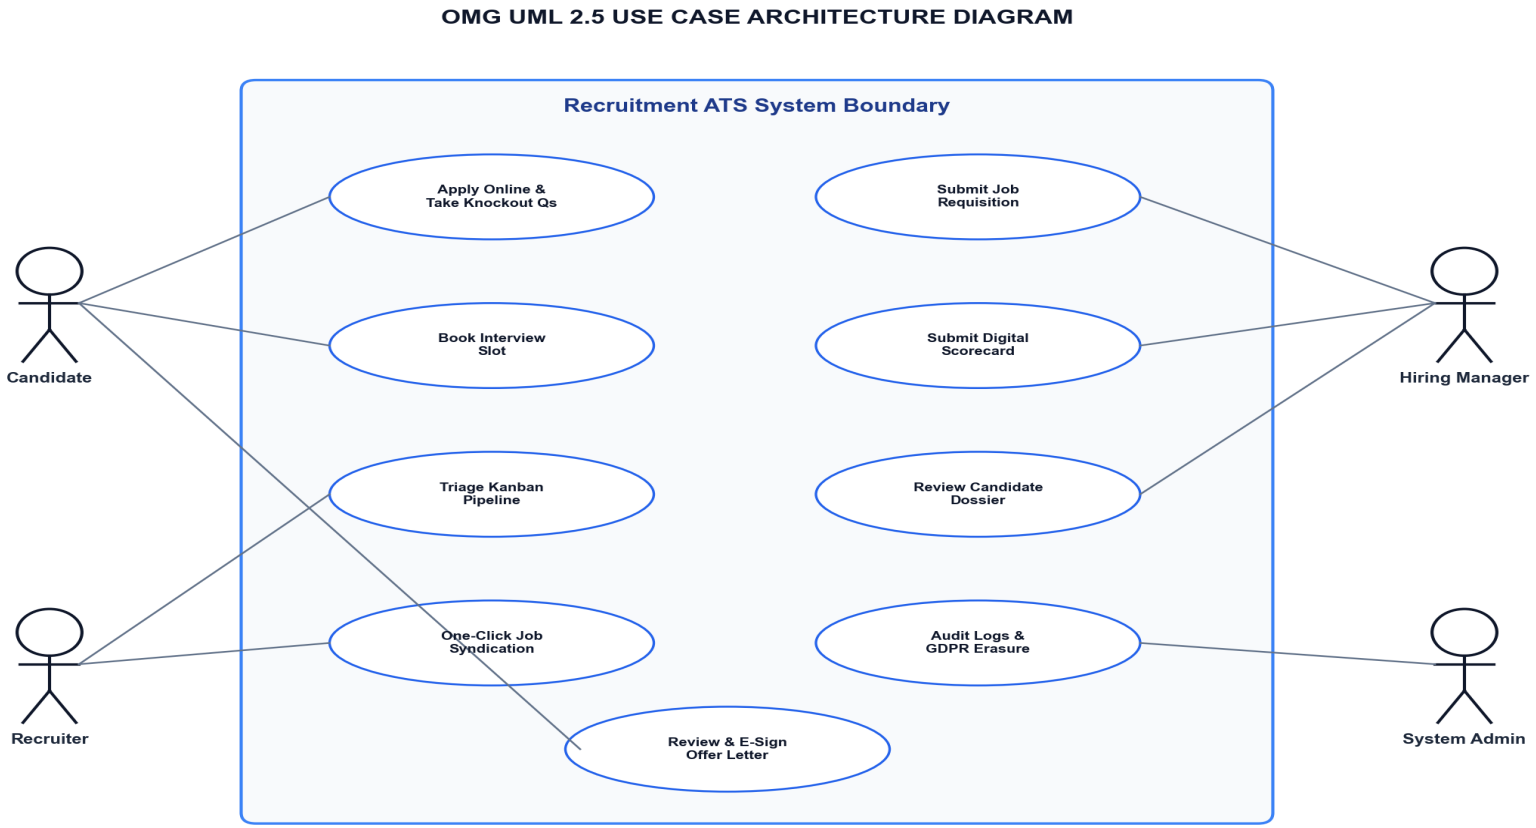

Core Modules: Requisition Governance | Sourcing & Parsing | Pipeline Management | Scheduling & Evaluation | Offer & Onboarding.

Enterprise Data Model: Relational Entity Architecture

Normalized 3NF relational schema enforcing strict referential integrity, auditability, and analytics readiness.


ENTITY-RELATIONSHIP DIAGRAM (3RD NORMAL FORM RELATIONAL SCHEMA)



Core Relational Entities: Requisition (1:N) Applications (1:N) Interviews (1:N) Scorecards (1:1) Offers (1:1) Hires.

System Architecture: Cloud-Native Microservices (C4 Container)


Event-driven architecture with resilient asynchronous integrations (Kafka, REST, Webhooks).

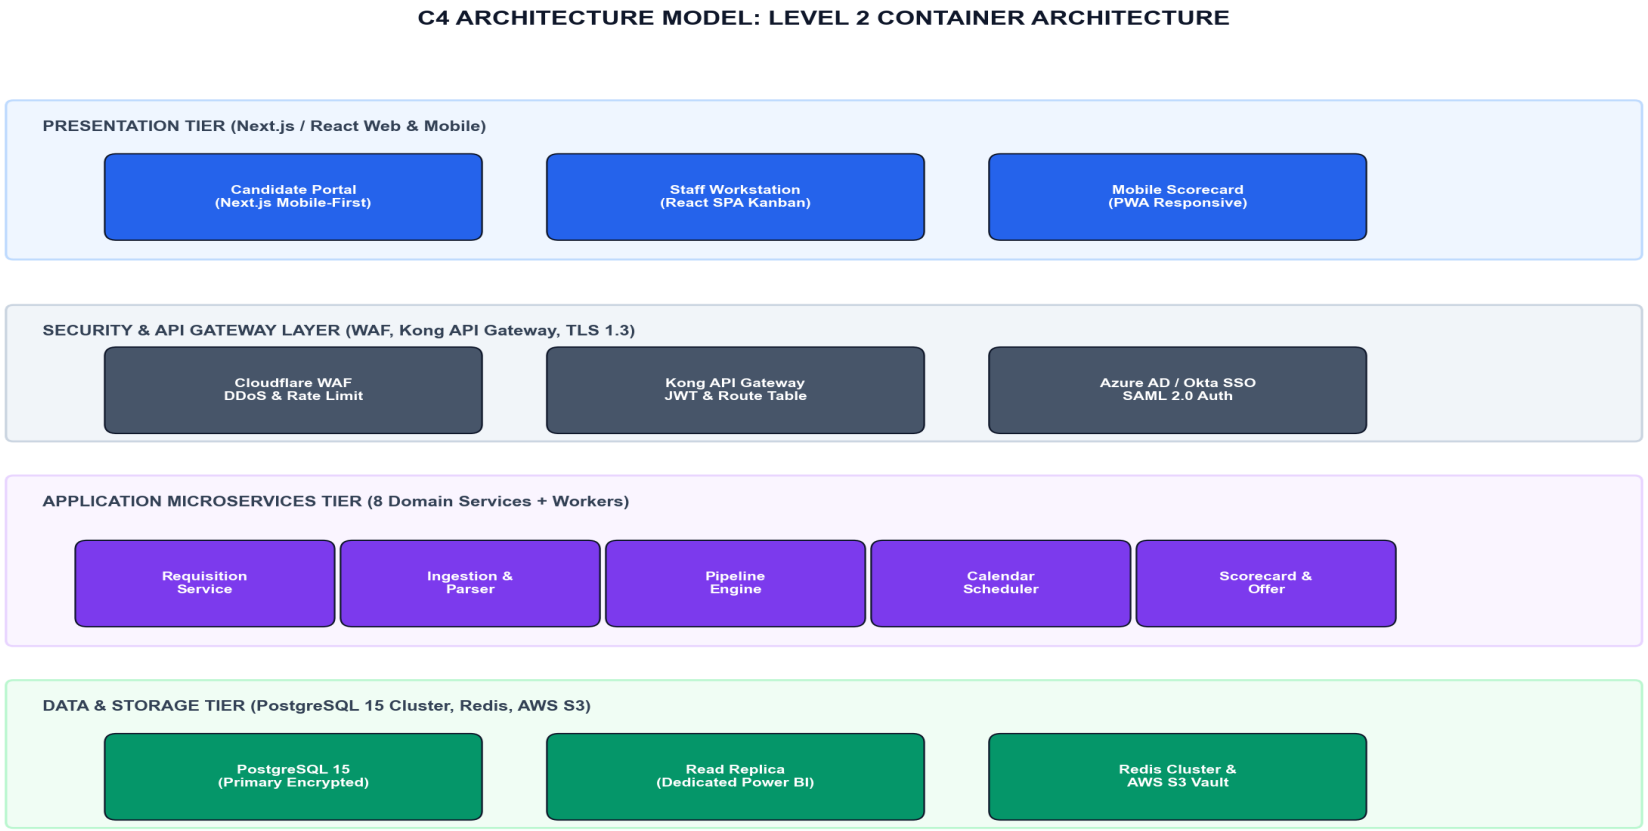

Enterprise Connectors: Workday HRIS | Google Workspace / Outlook 365 | LinkedIn / Indeed Job Boards | DocuSign e-Sign.

Data Analytics Framework: Funnel Velocity & KPIs

Power BI telemetry tracking 1,250 candidates across stage conversion, cost, and sourcing ROI.

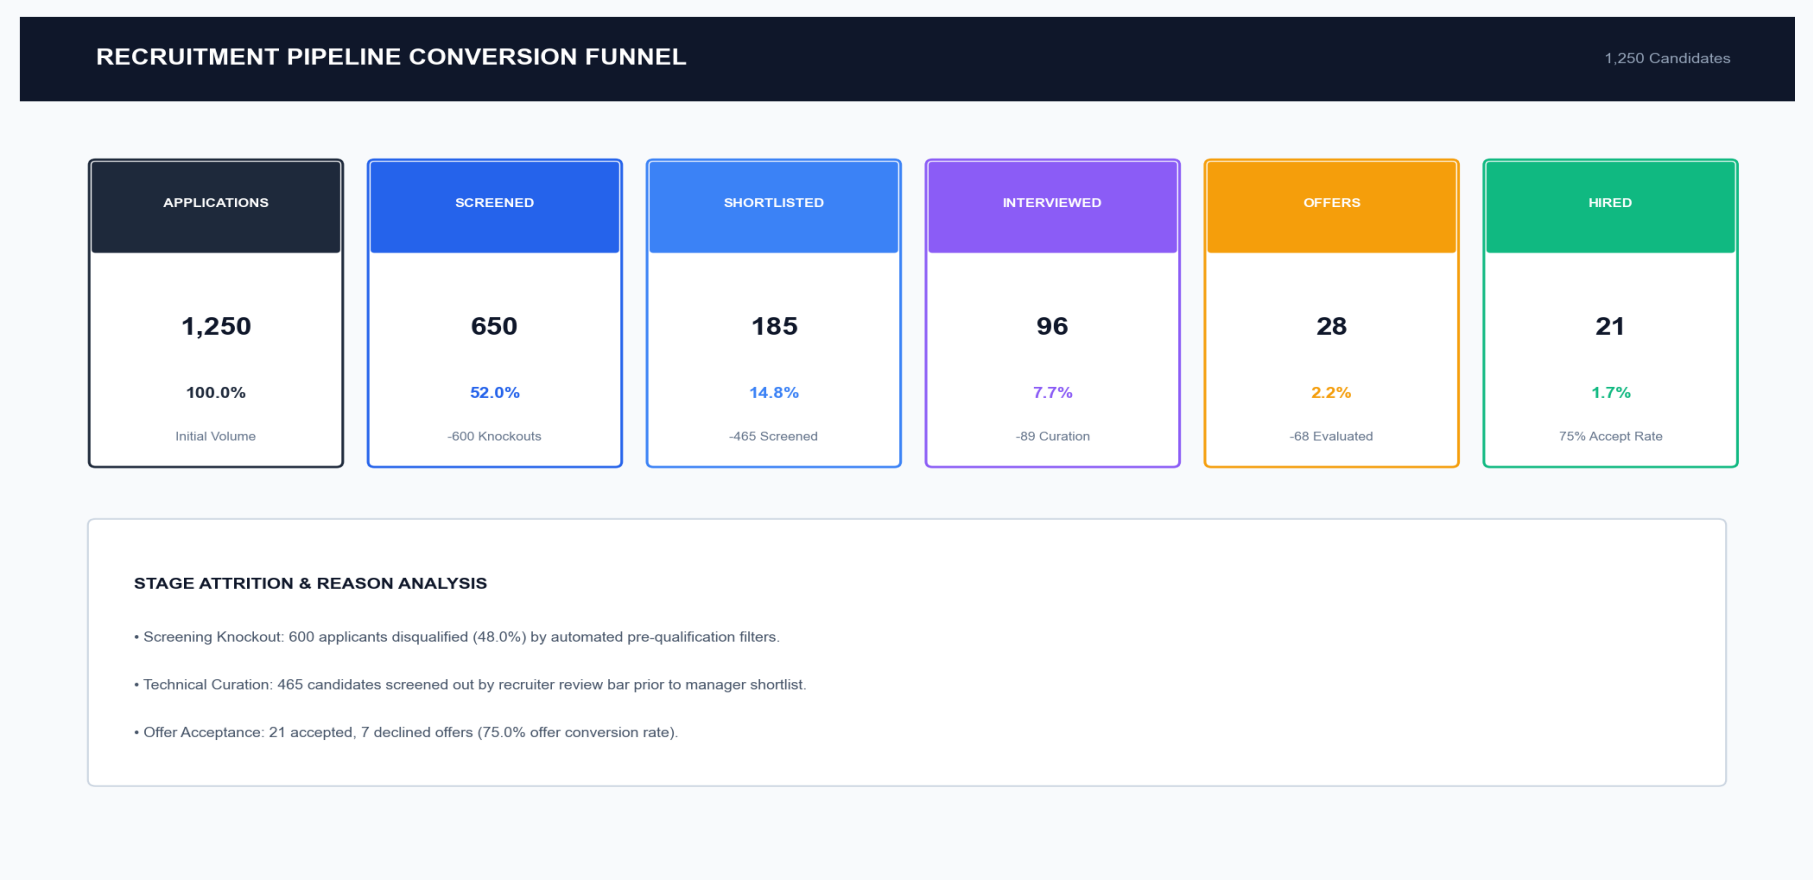

Dataset Insights: 1,250 Applicants -> 650 Screened (52%) -> 185 Shortlisted (28%) -> 96 Interviewed (52%) -> 28 Offers -> 21 Hires (75% Acceptance).

Phased Implementation Roadmap & Change Enablement

Structured 24-week rollout minimizing disruption, ensuring data integrity and high user adoption.

Phase & Duration	Core Scope & Key Deliverables	Milestone & Gate Criteria
Phase 1: Foundation (Weeks 1 - 6)	• Infrastructure setup, RDS PostgreSQL provisioning, Kafka event bus • Core Workday HRIS & Active Directory SSO integration • RBAC security matrix & data dictionary baseline	Gate 1: SSO & Workday Master Data Sync validated in Sandbox.
Phase 2: Core ATS (Weeks 7 - 14)	• Requisition management, automated resume intake & parsing • Interactive Recruiter Kanban pipeline & interview calendar sync • Mobile scorecard rubric & e-Signature integration	Gate 2: UAT sign-off by Talent Acquisition & Engineering Hiring Panel.
Phase 3: Rollout & Analytics (Weeks 15 - 24)	• Power BI executive dashboard deployment & data pipeline sync • Pilot rollout with Engineering & Sales departments • User training, change management enablement, enterprise cutover	Gate 3: 100% production cutover & legacy spreadsheet decommissioning.

Change Management Strategy: Role-based training workshops (Recruiters, Hiring Managers, HR Ops), quick-reference job aids, and proactive feedback loops.

Business Value, Financial ROI & Final Recommendation

Compelling economics: $525,000 net annual savings, 3.4x 3-year ROI, and 7.2-month payback.

Financial Returns	Operational Outcomes	Strategic Advantage
• Agency spend reduced by 60% ($290k/yr) • Recruiter productivity up 40% ($150k/yr) • Scheduling labor reduced 80% ($85k/yr) • **Total Net Benefit: $525,000 / year** • Implementation Capex: $210,000 • Payback Period: **7.2 Months**	• Time-to-Hire slashed from 42 to **21 Days** • Candidate drop-off cut from 38% to **12%** • Scorecard turnaround from 3.8d to **< 24h** • Offer acceptance rate lifted to **75%+** • Candidate NPS increased from +12 to **+65**	• Enterprise compliance with full EEO audit logs • Automated candidate rediscovery database • Competitive advantage in securing top tech talent • Scalable architecture supporting 500+ hires/yr

Recommendation: Approve Phase 1 capital expenditure ($210k) to commence infrastructure build and Workday integration.
